SEALED PROPOSAL • WEBSITE REDESIGN SERVICES

A clearer path to **county services.**

Website redesign and development proposal
County of Lee, Virginia

A working Lee County prototype, a migration-ready public record archive, and a practical plan to launch.

Prepared for

CLINT CARTER, COUNTY ADMINISTRATOR

Lee County Courthouse • Room 111
33640 Main Street • Jonesville, Virginia 24263

Prepared by

DYLAN SMITH • INDEPENDENT WEB DEVELOPER

dylanjsmith.dev@gmail.com
October 5, 2026

RFP issued September 21, 2026
Proposal due October 15, 2026 at 2:00 p.m. ET

Proposal ID: LC-WEB-2026-01
Valid through December 31, 2026

EXECUTIVE RESPONSE

Designed around Lee County—not adapted after the award.

This response pairs a county-specific working prototype with a disciplined completion plan for search, migration, accessibility, training, hosting, and launch.

October 5, 2026

Clint Carter, County Administrator
County of Lee, Virginia
P.O. Box 367
Jonesville, Virginia 24263

Re: Proposal for Website Redesign Services

Dear Mr. Carter:

I am pleased to submit this proposal to redesign and develop Lee County's public website. Rather than respond with a generic template or a collection of promises, I began with the County's actual information: its departments, public notices, meetings, documents, calendar needs, and local identity. The result is a working prototype that gives the County a concrete product to evaluate before making an award.

The proposed site is organized around the questions residents bring to county government: where to find a service, how to contact an office, when a meeting will occur, how to review an agenda or minute book, where to locate an official notice, and how to submit or update public information. Its visual system uses Lee County's seal, landscape, and established civic character while keeping government information direct and easy to scan.

A lower-risk starting point

The prototype already includes a responsive public interface, department and service pathways, an administrative publishing area, current-notice workflows, a moderated calendar, and a structured Board of Supervisors archive. The remaining work is clearly identified and tied to milestones, demonstrations, and County acceptance.

The recommended fixed-fee implementation estimate is $23,750, with a projected 10-week turnaround from notice to proceed and receipt of required content/access. The County may select optional hosting, ongoing support, or additional digital services separately.

Thank you for considering this locally informed, working-first approach. I welcome a technical demonstration and a line-by-line scope review with County staff.

Respectfully submitted,

Dylan Smith
Independent Web Developer
dylanjsmith.dev@gmail.com

WHAT LEE COUNTY RECEIVES

A public-service website with a practical operating model.

The project is not limited to a visual refresh. It includes the content structure, staff tools, migration process, quality controls, training, and post-launch support needed to keep the site useful.

01	**Findability**	Task-based navigation, prominent search, department landing pages, cross-content results, and clean URLs.
02	**Transparency**	Notices, bids, calendars, agendas, minutes, audio, budgets, and documents organized for public access.
03	**County control**	Role-based publishing tools let authorized staff post, review, schedule, expire, and maintain content in-house.
04	**Migration confidence**	Inventory, mapping, metadata cleanup, automated imports, manual review, redirect planning, and acceptance reports.
05	**Inclusive access**	Responsive layouts, keyboard support, semantic markup, accessible documents guidance, and WCAG 2.2 AA validation.
06	**Durable operations**	Managed hosting, security controls, backups, monitoring, documentation, training, and support options.

Proposal organization

- RFP compliance and implementation status
- User experience, information architecture, CMS, search, SEO, and hosting
- Data and file migration, testing, accessibility, security, and launch
- Training, ongoing support, project team, qualifications, references disclosure, cost, and terms
- Submission checklist and signature page

RFP COMPLIANCE

A direct response to the County's stated objectives.

Every preliminary scope item and development objective is addressed below. Status labels distinguish demonstrated prototype work from contract completion work.

RFP requirement	Proposed response	Status
Highly usable, dynamic design	Task-first home page, service pathways, responsive components, department templates, and clear calls to action.	Prototype + refine
Transparency and customer service	Prominent access to notices, bids, meetings, minutes, audio, budgets, calendars, contacts, and documents.	Prototype
Marketing, news, projects, events	County-branded hero, update cards, event calendar, public notices, optional project pages and alerts.	Prototype + content
Consolidate and migrate content	Crawl/inventory, content map, automated file import, metadata cleanup, manual QA, and 301 redirect register.	Planned + partial
Department and community needs	Department discovery interviews, repeatable templates, service directory, shared publishing standards.	Planned
Government look + unique presence	Lee County seal, local landscape, forest/gold palette, readable civic typography, restrained motion.	Prototype
Navigation and department pages	User-centric menus, breadcrumbs, quick links, department landing pages, related resources, search.	Prototype + content
Desktop, tablet, mobile; browsers	Responsive implementation; current and previous major browser versions; device test matrix before acceptance.	Prototype + QA
Hosting	Managed static/application hosting, database and file storage, SSL, backups, monitoring, and domain cutover.	Proposed
SEO and smart site search	Indexable HTML, sitemap, metadata, schema, PDF text indexing, typo tolerance, phrase search, relevance, and facets.	Interface exists; engine planned
Knowledge transfer and training	Admin guide, live role-based sessions, recordings, quick-reference sheets, sandbox exercises, 30-day support.	Proposed
In-house posting and maintenance	Authenticated admin workspace for pages, notices, documents, meetings, and calendar moderation.	Prototype + refine


Scope boundary honored

Constitutional Officers and the Lee County Economic Development Authority remain on their separate websites. The redesigned site will provide clear, maintained outbound links and context without migrating or duplicating those sites.

DEMONSTRATED PROGRESS

The County can evaluate real work now.

The current prototype establishes the visual direction and validates key publishing and public-record workflows before contract award.

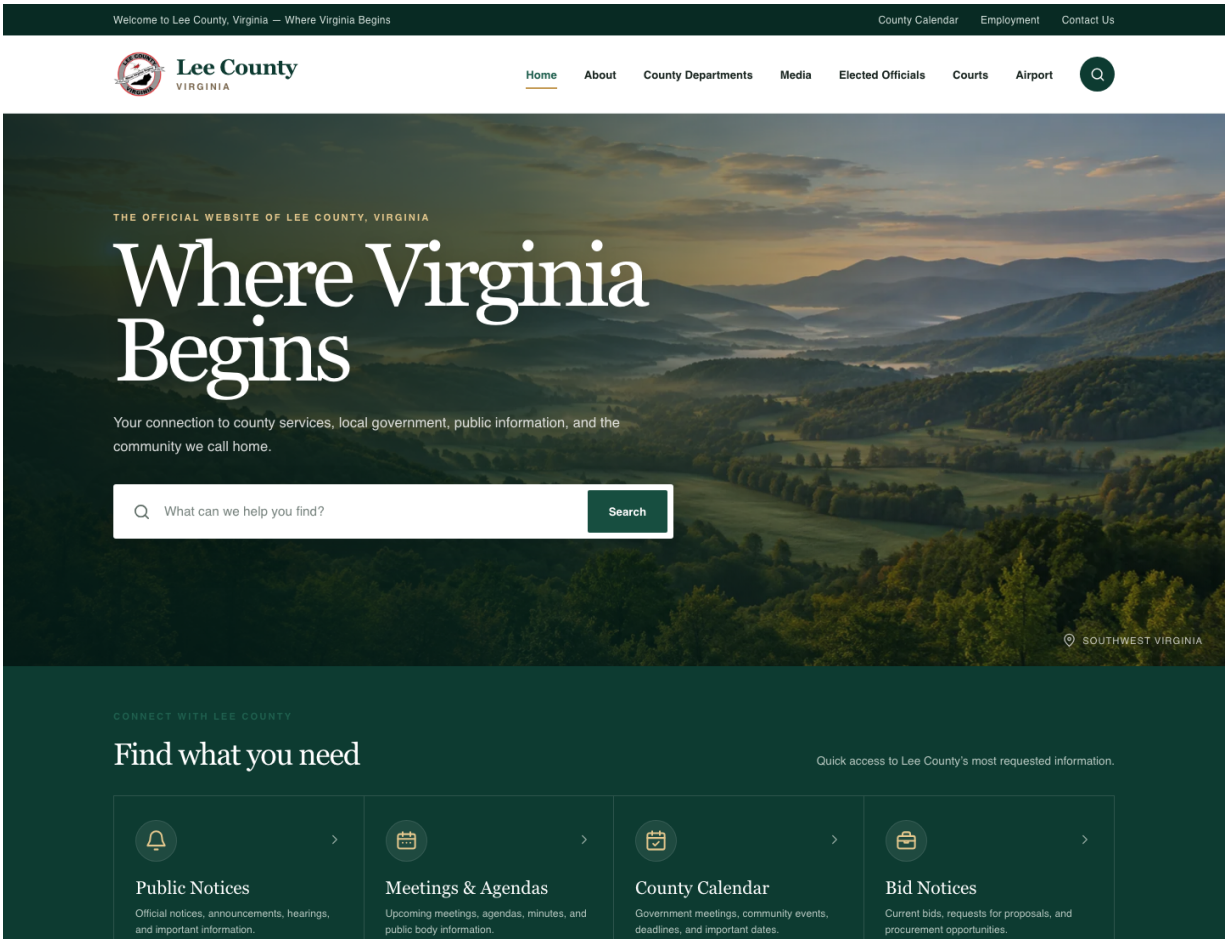

Working prototype: public home page with county identity, task-oriented navigation, prominent search entry, and quick access to high-demand content.

678	519	152	2016–2026
ARCHIVE FILES	PDF RECORDS	AUDIO RECORDS	YEARS ORGANIZED

Verified prototype capabilities


- Public notice presentation with deadlines, expiration, featured status, contacts, links, and PDF attachments.
- Meeting archive organized by year, meeting type, record type, and keyword, with agendas, minutes, and audio.
- Document library and staff upload/publishing workflows backed by authenticated storage permissions.
- County calendar with public single-event and CSV submissions, validation, review, approval, rejection, and publishing.
- Administrative workspace for notices, meeting records, county documents, and event moderation.

- Successful production build and clean lint result as of October 5, 2026.

DEMONSTRATED PROGRESS

A public record archive built for the way people look for meetings.

The archive is more than a folder of files: it presents a predictable year-based view and supports filtering by document type, meeting type, and search terms.

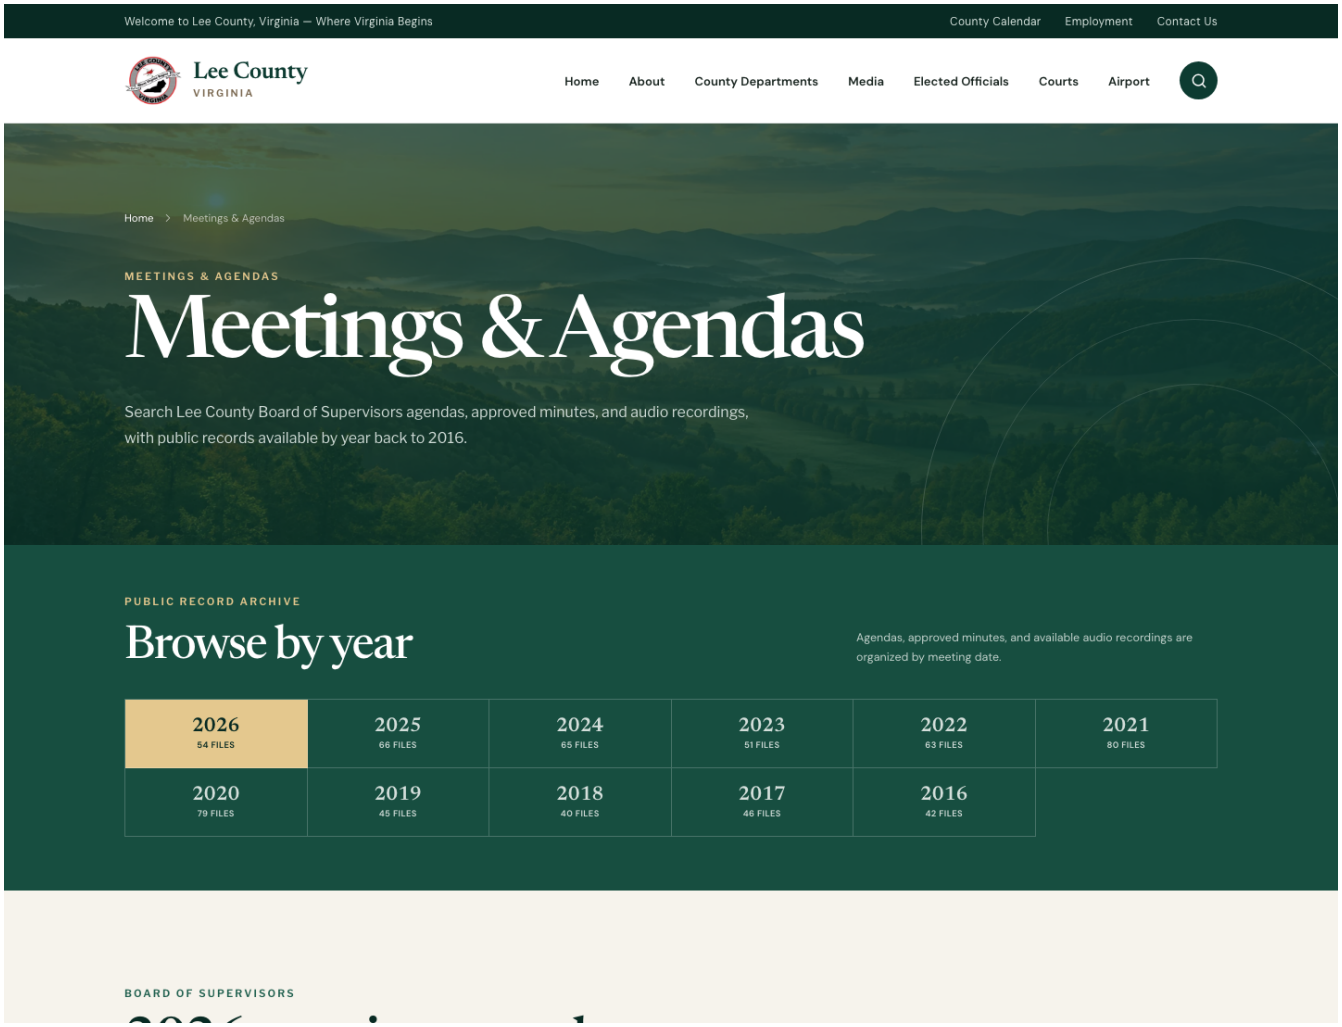

Working prototype: Board of Supervisors records organized by year, with document counts and public-facing archive context.

Prototype is evidence—not a claim of completion

The homepage search field currently demonstrates placement and interaction only. Contract work includes the production search index, PDF text extraction, typo tolerance, exact-phrase behavior, relevance tuning, content-type filters, analytics, and result-page accessibility required by the RFP.

Acceptance evidence at each milestone

- A working URL on a protected staging environment
- A written requirement/status register and issue log

- Demonstrations using County content and realistic staff tasks
- Migration counts, broken-link checks, redirect register, browser/device results, and accessibility findings
- County sign-off before production cutover

USER EXPERIENCE

Organized around resident tasks and staff ownership.

The navigation model balances a stable government structure with direct paths to the information residents request most often.

Audience	High-value tasks	Design response
Residents & property owners	Services, forms, payments, notices, meetings, property/GIS, contacts	Plain-language service paths, search, quick links, printable details
Businesses & applicants	Permits, zoning, bids, development, employment	Topic pathways, department ownership, requirements and next steps
Visitors & community groups	Events, airport, tourism links, community resources	Calendar, external partner links, location and contact context
County staff	Post, revise, schedule, approve, expire, archive	Role-based admin, structured fields, previews, publishing states
Search engines & assistive tech	Understand content and relationships	Semantic HTML, metadata, schema, headings, landmarks, alt text

Proposed top-level structure

County Government	Administration • Board of Supervisors • departments • elected officials • courts • county code
Services	Building & inspections • zoning • mapping/GIS • recycling • forms • payments • employment
Public Information	Notices • meetings • agendas • minutes • audio • bids • budgets • reports • policies
Community	Calendar • airport • tourism • economic development • local and regional resources

Discovery decision points

During kickoff, County staff will confirm top tasks, department owners, emergency publishing needs, required forms/integrations, records-retention expectations, approval roles, analytics goals, and which legacy pages should be rewritten, archived, redirected, or retired.

CMS AND TECHNICAL APPROACH

Modern delivery without making routine updates technical.

The recommended architecture separates the fast public website from authenticated content management, structured data, and document storage. County staff work in forms and previews—not source code.

PUBLIC EXPERIENCE	CONTENT & WORKFLOW	OPERATIONS
Responsive React interface Department and topic templates Accessible components Search results and filters	Supabase/PostgreSQL CMS Role-based sign-in Draft, review, publish, expire Documents and media storage	Managed hosting + SSL Backups and monitoring Analytics + error tracking Deployment and rollback

Content types and controls

Content type	Structured fields and workflow
Department/service pages	Owner, contact, overview, services, documents, related links, alerts, review date
Public notices and bids	Type, summary, body, posted/deadline/expiration dates, contact, submission details, attachment, featured flag
Meetings and records	Public body, meeting type/date, agenda/minutes/audio, publication state, accessible title and metadata
Calendar events	Schedule, all-day option, venue/address, category, link, description, submitter contact, moderation status
Documents	Category, title, description, document date, department, file, visibility, keywords, replacement/version notes

- Least-privilege accounts and role checks for authorized County staff
- Preview before publishing and clear status labels
- Required-field, file-type, file-size, date, and URL validation
- Automatic expiration for time-sensitive notices and event moderation for public submissions
- Audit-friendly created/updated timestamps and accountable user identity
- Exportable structured data and County ownership of content and uploaded files

SEARCH AND DISCOVERY

One search across pages, documents, events, and news.

The production search experience will satisfy the RFP's detailed requirements and will be tested with real Lee County vocabulary, common misspellings, acronyms, and service questions.

Capability	Implementation and acceptance measure
HTML + PDF indexing	Index published pages and extract searchable text/metadata from supported PDFs; exclude private or unpublished content.
Single words, multiple words, phrases	Support broad terms, combined terms, and quoted exact phrases; document expected behavior in help text.
Typo tolerance	Return useful best matches for common misspellings while allowing users to view the original query.
Relevance	Weight titles, service names, department, metadata, headings, body content, freshness, and curated synonyms.
Facets	Filter by pages, documents, meetings, events, notices/news, department, category, and year where appropriate.
Accessible results	Keyboard-operable filters, clear result counts, query announcement, highlighted context, and meaningful empty states.
Search analytics	Track zero-result and frequently used queries without collecting unnecessary personal information.

Search engine optimization

- Crawlable, server-delivered or pre-rendered public HTML; XML sitemap; robots controls; canonical URLs; clean redirects.
- Unique titles, descriptions, headings, social-sharing metadata, image descriptions, and appropriate structured data.
- Descriptive document filenames and metadata, text-based PDFs where available, and accessible alternatives for scanned files.
- Fast pages with optimized images, restrained scripts, cache policies, and Core Web Vitals monitoring.
- Google Search Console and Bing Webmaster Tools setup, verification, sitemap submission, and launch monitoring.

Content quality affects ranking

Technical SEO will be paired with plain-language page titles, clear service descriptions, local terminology, current contact information, and a review schedule so the County's most useful pages remain discoverable.

DATA AND FILE MIGRATION

Preserve the County's investment—and improve it during the move.

Migration will be managed as a countable, reviewable workstream rather than an untracked copy-and-paste exercise.

Phase	Activities	Evidence delivered
1. Inventory	Crawl public URLs; enumerate pages, files, media, forms, redirects, owners, dates, and known external systems.	Source inventory + baseline counts
2. Decide	Mark each item keep, revise, merge, archive, link externally, or retire; map it to the new structure and owner.	Approved content map
3. Prepare	Normalize filenames, dates, titles, categories, document types, alt text, and required metadata; flag scans and duplicates.	Clean import sheets + exception list
4. Import	Use scripts and structured imports for repeatable content; manually create content where automation would reduce quality.	Import logs + record counts
5. Validate	Compare source/target counts, sample every content type/year, test files and links, check permissions, and review mobile display.	Migration QA report
6. Redirect	Map priority and changed URLs to their best new destinations; identify intentional removals and external links.	301 redirect register
7. Freeze & delta	Agree on a brief content freeze, capture late changes, run final delta import, and obtain County acceptance.	Final reconciliation + sign-off

Archive advantage

The working prototype already organizes 2016–2026 Board of Supervisors records and contains 678 locally staged archive files. That work becomes the foundation for final deduplication, naming cleanup, missing-record review, accessibility triage, and production import.

Migration assumptions

- Base pricing includes migration and validation of up to 750 existing documents/files plus agreed page content in the final site map.
- The County supplies administrator access or source exports and identifies authoritative versions where duplicates conflict.
- Remediation of complex inaccessible legacy PDFs is prioritized and estimated separately after inventory; simple naming and metadata cleanup is included.
- Third-party systems remain linked or embedded unless the final scope explicitly includes an integration or replacement.

QUALITY AND PUBLIC TRUST

Accessibility, security, privacy, and performance are acceptance criteria.

The site will be evaluated through automated checks, keyboard and screen-reader review, representative user tasks, browser/device testing, and documented County acceptance.

Area	Commitment	Launch evidence
Accessibility	Target WCAG 2.2 Level AA and Section 508-aligned practices: semantic structure, contrast, focus, keyboard access, labels, errors, captions/transcripts planning, reduced motion, zoom/reflow.	Audit findings, remediation log, manual checklist
Responsive/browser	Current and one prior major version of Chrome, Edge, Firefox, and Safari on representative Windows, macOS, iOS, and Android sizes.	Browser/device matrix and issue disposition
Performance	Optimized media, caching, code splitting, font strategy, request control, and Core Web Vitals review on representative pages.	Performance report and documented exceptions
Security	TLS, least privilege, row-level data rules, restricted storage, secure authentication, dependency review, backups, update process, rate/abuse controls where needed.	Configuration checklist and recovery test
Privacy	Data minimization, private submitter contacts, no public exposure of admin information, cookie-light analytics option, privacy notice support.	Data-flow review and privacy configuration
Content quality	Broken-link review, spelling and metadata checks, owners/review dates, consistent dates/addresses/phone formats, useful 404 page.	QA checklist and owner register

Launch readiness gates

- No unresolved critical security or accessibility defect
- County approves navigation, design, priority content, and migrated record counts
- Production search indexes all agreed public content and passes agreed query scenarios
- Backups, restore/rollback plan, domain/DNS responsibilities, analytics, and monitoring are confirmed
- Administrators complete training exercises and receive documentation
- Launch communications, freeze window, go/no-go contacts, and rollback decision are documented

PERFORMANCE TIMELINE

Ten weeks from notice to proceed to launch.

The schedule assumes timely access to source content, weekly County feedback, and decisions within two business days for milestone approvals. Existing prototype work permits design and migration tasks to overlap.

Timing	Milestone	Key work and County checkpoint
Week 1	Kickoff & discovery	Confirm goals, stakeholders, owners, integrations, metrics, risks, governance, access, and communications.
Weeks 1–2	Inventory & information architecture	Crawl legacy site, baseline content, confirm user tasks, approve new site map and migration decisions.
Weeks 2–3	Design validation	Review prototype, refine responsive components, department templates, accessibility patterns, and visual details.
Weeks 3–6	CMS & frontend completion	Finish content models, permissions, publishing flows, page templates, production search, SEO, and integrations.
Weeks 4–7	Migration	Normalize, import, deduplicate, categorize, link, and validate pages and files; build redirect register.
Weeks 7–8	QA & UAT	Accessibility, device/browser, performance, security, link, forms, search, and staff acceptance testing.
Week 9	Training & launch readiness	Admin training, documentation, final delta migration, DNS/hosting rehearsal, go/no-go review.
Week 10	Production launch	Cutover, smoke testing, indexing checks, monitoring, public handoff, and stabilization begins.
30 days after	Stabilization & closeout	Resolve warranty issues, tune search, review analytics, deliver final artifacts and closeout report.

Average turnaround commitment

The projected turnaround is 10 calendar weeks after notice to proceed and receipt of required credentials/content. A compressed schedule may be negotiated after discovery; content-access or approval delays move dependent dates day-for-day.

Project communication

- One accountable project contact and one County product owner
- Weekly 30-minute progress review with decisions, risks, upcoming tasks, and demonstration
- Shared action/decision log and milestone acceptance checklist
- Prompt escalation of content, access, scope, or schedule risks

KNOWLEDGE TRANSFER AND SUPPORT

County staff leave able to operate the site.

Training uses County content and job-based scenarios. Staff will practice the work they actually perform, receive concise references, and retain a sandbox or staging environment for safe rehearsal.

Audience	Session	Topics and deliverables
Content contributors	90 minutes	Edit pages, links, contacts, accessibility basics, images, documents, previews, drafts, and review dates.
Publishers/department leads	90 minutes	Approve and publish, schedule/expire notices, manage department content, quality checks, and corrections.
Clerk/records staff	90 minutes	Post meetings, agendas, minutes, and audio; use naming/metadata standards; replace or correct a record.
Calendar moderators	60 minutes	Review public submissions, validate contacts/details, approve/reject/edit, publish, and manage CSV uploads.
Site administrators	2 hours	Users/roles, content types, storage, backups, analytics, incident escalation, configuration boundaries, and vendor support.

- Live remote sessions for up to 12 staff members; recordings supplied for internal use
- Administrator handbook, quick-reference sheets, publishing checklist, and content style guide
- One follow-up office-hour session during the 30-day stabilization period
- Help requests acknowledged within one business day during implementation and stabilization

Ongoing service options

Service	Included response	Monthly price
Essential care	Up to 3 hours; routine updates, dependency review, uptime/backup check; 2-business-day response	$275
Standard support	Up to 8 hours; content/development help, monthly report, accessibility/search review; 1-business-day response	$625
Priority partnership	Up to 16 hours; priority queue, quarterly roadmap, staff office hour; 4-business-hour response	$1,200
As-needed support	Scheduled development, training, or content assistance without retainer	$110/hour

Emergency response and after-hours work are subject to availability and quoted at $150/hour. Service-level terms, rollover, exclusions, and escalation contacts will be stated in the final agreement.

QUALIFICATIONS AND PROJECT TEAM

One accountable lead from discovery through training.

Dylan Smith will serve as project manager, user-experience designer, frontend/backend developer, migration lead, quality coordinator, trainer, and primary support contact.

Responsibility	Relevant capability and demonstrated evidence
Project management	Milestone planning, requirement tracking, decision logs, weekly demonstrations, scope/risk reporting, and acceptance checklists.
Design and frontend	Responsive React/Vite interface, county-specific visual system, semantic components, navigation, search entry, templates, and administrative forms.
Data and CMS	Supabase/PostgreSQL content models, authenticated administration, row-level policies, restricted file storage, validation, publishing states, and CSV workflows.
Migration	Archive indexing scripts, repeatable import tooling, content normalization, metadata mapping, file organization, reconciliation, and exception reporting.
Training and support	Role-based demonstrations, written setup/operations guidance, staff workflow documentation, and post-launch stabilization.

No subcontracting planned

No subcontractor is included in this proposal. If a specialist becomes advisable—for example, professional translation, complex PDF remediation, or penetration testing—no subcontracted work will begin without written County identification and acceptance.

Documented work samples

Work sample	Relevance
Lee County working prototype	County-specific navigation, services, notices, bids, meeting records, document management, calendar submissions/moderation, administrative publishing, and local visual identity.
Discover Lee VA — discoverleeva.com	Related community/tourism platform work, including event publishing and CSV intake, business and artisan directory workflows, managed content, and public-facing local information.

Required factual completion

Before the sealed response is delivered, insert the proposer's exact number of years in business, exact years of professional website design/development experience, telephone number, and mailing address. Those facts were not present in the supplied project materials and have not been invented in this proposal.

REFERENCES DISCLOSURE

A candid exception, paired with stronger project controls.

The RFP requests at least five county/municipality references, preferably including two in Virginia. The proposer does not currently have those government-agency references and does not present unrelated contacts as government clients.

Requested exception

The proposer respectfully asks Lee County to evaluate the working prototype, technical demonstration, related community platform, milestone-based payment plan, acceptance gates, and warranty as substitute evidence of competence, and—if the County determines it appropriate—to exercise its reserved right to waive this deviation. The proposer understands the County may instead determine that the reference requirement is material and decline the proposal.

Risk-reduction commitments

County concern	Proposed protection
Can the proposer deliver the stated user experience?	County evaluates a working Lee County prototype and receives a staged URL at every major milestone.
Will the CMS work for staff?	Staff complete defined publishing tasks in staging before CMS acceptance and related payment.
Will legacy records be preserved?	Baseline counts, mapping decisions, import logs, sampling, reconciliation, and County sign-off are required.
Will the site be usable and accessible?	Test matrix, accessibility remediation log, search scenarios, browser results, and UAT are acceptance deliverables.
What happens if progress stops?	Milestone payments limit County exposure; County receives paid-for deliverables, content, data exports, and current documentation.
What happens after launch?	Thirty-day defect stabilization is included, with optional support plans and documented handoff.

Permitted substitute references

If the County will accept non-government references, up to five client or professional contacts may be added here after the proposer obtains permission to share their names, organizations, telephone numbers, email addresses, project descriptions, and dates. No contact should be listed without consent.

Reference	Organization / project	Contact information
1	To be supplied with permission	Name • title • phone • email
2	To be supplied with permission	Name • title • phone • email
3	To be supplied with permission	Name • title • phone • email
4	To be supplied with permission	Name • title • phone • email

Reference	Organization / project	Contact information
5	To be supplied with permission	Name • title • phone • email

COST ESTIMATE

A fixed-fee core project with separately priced options.

Final scope will be confirmed with the County. The core estimate includes project management, design validation, development, CMS completion, migration within stated limits, search, SEO, QA, training, launch, and 30-day stabilization.

Core deliverable	Estimated fee
Discovery, requirements, governance, and project management	$2,250
Information architecture and responsive design validation	$2,750
Public frontend and staff CMS completion	$6,750
Content/file migration, metadata, QA, and redirects (up to 750 files)	$4,750
Production site search and technical SEO	$3,250
Accessibility, browser/device, performance, and security QA	$2,250
Training, launch, documentation, and 30-day stabilization	$1,750
TOTAL ESTIMATED FIXED FEE	**$23,750**

Proposed milestone payment schedule

Milestone	Percent	Amount
Contract / notice to proceed; kickoff and access checklist	15%	$3,562.50
Information architecture and design acceptance	20%	$4,750.00
Functional staging beta: CMS, templates, and search	30%	$7,125.00
Migration, QA, training, and launch-readiness acceptance	20%	$4,750.00
Production launch and start of 30-day stabilization	15%	$3,562.50

Invoices are due Net 15 unless the County's standard payment terms require otherwise. No interest, late fee, or reimbursable travel cost is included without a final written agreement. Material scope changes require a written change request stating cost and schedule impact before work begins.

OPTIONAL PRODUCTS AND SERVICES

Useful additions the County may accept now or later.

Options are independent of the core project unless selected in writing. Third-party fees and final requirements may affect quoted amounts.

Optional service	Estimated cost
Managed production hosting, SSL, backups, uptime monitoring, and routine platform oversight	$95/month ($1,140/year)
Accessibility monitoring dashboard and quarterly issue review	$900/year
Analytics/search-insight dashboard with quarterly summary	$1,200 setup
Emergency banner and department-level alert workflow	$850
Email subscription / notice digest integration	$1,500 + provider fees
SMS alerts integration	$1,800 + messaging fees
Online service-request intake with routing and status notifications	From $2,750
Multilingual framework and priority-page publishing workflow	$1,800 + translation
Additional legacy file migration above included 750	$3/file; minimum $300
Simple page copyediting / plain-language rewrite	$90/page
Complex legacy PDF accessibility remediation	After inventory; from $65/file
Additional onsite or remote training	$110/hour + approved travel
Independent penetration test coordination	Third-party quote + coordination

Recommended future roadmap

- Phase 2: searchable staff directory, online service request routing, and emergency banner controls
- Phase 2: email/SMS subscriptions for notices, bids, meetings, and calendar categories
- Phase 3: priority form digitization, payment/integration review, and GIS or property-data connections
- Ongoing: quarterly accessibility, search, content-freshness, and analytics reviews

Avoid unnecessary subscriptions

The final architecture will favor portable data, open web standards, and the smallest practical set of paid services. Any recurring platform or search license will be identified for County approval before commitment.

ASSUMPTIONS, OWNERSHIP, AND COMMITMENTS

Clear boundaries protect the County and the schedule.

Topic	Proposed term
County responsibilities	Designate a product owner; provide timely content/access; identify authoritative records; coordinate department review; make decisions; review milestones; control domain/DNS and legal policy content.
Included revisions	Two consolidated review rounds for site architecture/design and one consolidated review round per major template before acceptance. Defects and missed requirements are corrected without consuming revisions.
Ownership	Upon full payment, the County owns its content, uploaded files, structured data, approved custom design artifacts, and custom project code, subject to third-party open-source licenses. Proposer retains pre-existing general tools and know-how.
Credentials and portability	Production service accounts should be County-owned wherever practical. Credentials are transferred through an agreed secure method; data exports and current documentation are supplied at closeout.
Warranty	For 30 calendar days after launch, the proposer will correct reproducible defects that cause accepted requirements to fail, at no additional professional-services charge.
Third-party services	Licenses, transaction fees, domain costs, translation, professional photography, complex document remediation, and integrations not listed in the core estimate require County approval.
Records and legal review	County determines Virginia public-records, retention, privacy, open-meetings, procurement, and legal-policy requirements. The proposer configures agreed technical controls but does not provide legal advice.
Subcontracting	None planned. Any future subcontractor must be identified and accepted in writing by the County before performing work.
Non-discrimination	By signing and submitting, the proposer covenants not to discriminate in employment on the bases stated in the RFP, including race, color, religion, national origin, age, sex, marital status, or unrelated disability.

This proposal is an offer to negotiate a final scope and agreement; it does not override the RFP or the County's lawful terms. If a conflict exists, the executed agreement and incorporated procurement documents control.

SUBMISSION AND ACCEPTANCE

Final assembly checklist for the sealed response.

The RFP requires physical delivery. Email or fax submission is not accepted, and a postmark does not satisfy the deadline.

Complete	Required action
☐	Insert exact years in business and years of professional web design/development experience.
☐	Insert proposer telephone number and mailing address.
☐	Add permitted non-government references if available, or leave the candid exception disclosure unchanged.
☐	Review and approve the proposed $23,750 cost, options, payment milestones, and 10-week schedule.
☐	Sign the certification below; add any required W-9, business license, insurance, or vendor forms requested by the County.
☐	Print three complete hard copies and place one complete PDF electronic copy on a CD or flash drive.
☐	Seal all copies in one envelope/package marked with proposer name and “Proposal for Website Redesign Services.”
☐	Deliver no later than 2:00 p.m. ET, Thursday, October 15, 2026. Do not rely on a postmark.

Delivery address

BY MAIL	IN PERSON
Clint Carter, County Administrator P.O. Box 367 Jonesville, Virginia 24263	Clint Carter, County Administrator Lee County Courthouse 33640 Main Street, Room 111 Jonesville, Virginia 24263

Question deadline

Questions about the RFP must be directed to Clint Carter at ccarter@leecova.org no later than October 9, 2026. A prudent question is whether the County will accept substitute non-government references and the working prototype in place of five county/municipal references.

CERTIFICATION

Proposer acknowledgment and signature.

The undersigned certifies that the information in this proposal is accurate to the best of the proposer's knowledge, acknowledges the disclosed reference exception, agrees to the RFP non-discrimination covenant, and is authorized to negotiate the proposed services.

PROPOSER	Dylan Smith, Independent Web Developer
EMAIL	dylanjsmith.dev@gmail.com
TELEPHONE	_____
MAILING ADDRESS	_____ _____
SIGNATURE	_____
DATE	_____

Built around Lee County's information. Structured for the County's staff. Designed to make public service easier to find.

END OF PROPOSAL • LC-WEB-2026-01
